CITY OF CLEARWATER
NORTH MARINA DEVELOPMENT PLAN
APRIL 6, 2016
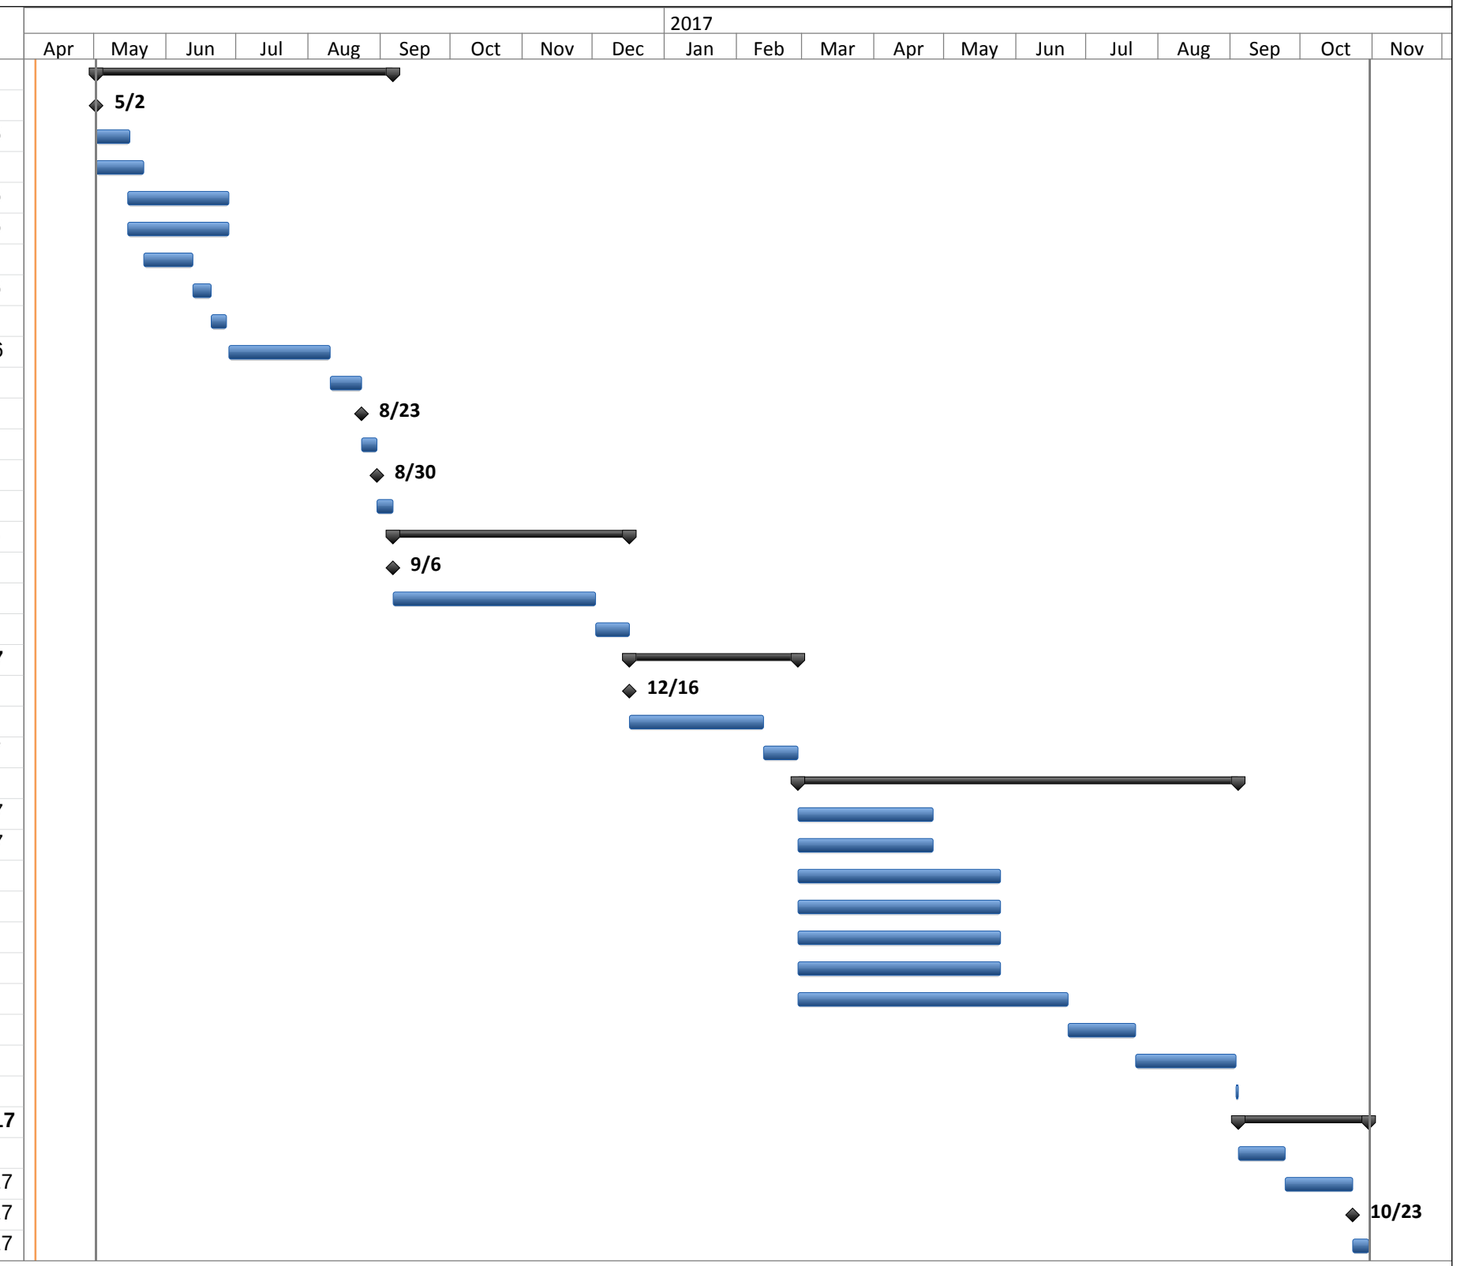
ID	Task Name	Duration	Start	Finish
1	**CONCEPTUAL DESIGN PHASE**	**132 days**	**Mon 5/2/16**	**Tue 9/6/16**
2	Kick-off Meeting	0 days	Mon 5/2/16	Mon 5/2/16
3	Site Inspection	15 days	Mon 5/2/16	Mon 5/16/16
4	Data Collection	21 days	Mon 5/2/16	Sun 5/22/16
5	Surveying	45 days	Sun 5/15/16	Mon 6/27/16
6	Geotechnical Investigation	45 days	Sun 5/15/16	Mon 6/27/16
7	Utility Coordination	22 days	Sun 5/22/16	Sun 6/12/16
8	Subsurface Utility Engineering (SUE)	8 days	Sun 6/12/16	Mon 6/20/16
9	Permitting Pre-application Meetings	7 days	Mon 6/20/16	Sun 6/26/16
10	Conceptual Plan Preparation	45 days	Tue 6/28/16	Wed 8/10/16
11	City Review of Conceptual Drawings	14 days	Wed 8/10/16	Tue 8/23/16
12	Review Comments from City	0 days	Tue 8/23/16	Tue 8/23/16
13	Plan Revisions	7 days	Wed 8/24/16	Tue 8/30/16
14	Public Meeting	0 days	Tue 8/30/16	Tue 8/30/16
15	Public Feedback Direction from City	7 days	Tue 8/30/16	Tue 9/6/16
16	**PRELIMINARY DESIGN PHASE**	**105 days**	**Tue 9/6/16**	**Fri 12/16/16**
17	Review Meeting with City	0 days	Tue 9/6/16	Tue 9/6/16
18	Prepare Preliminary Engineering Drawings	90 days	Tue 9/6/16	Fri 12/2/16
19	City Review of Preliminary Drawings	15 days	Fri 12/2/16	Fri 12/16/16
20	**FINAL DESIGN PHASE**	**75 days**	**Fri 12/16/16**	**Mon 2/27/17**
21	Review Meeting with City	0 days	Fri 12/16/16	Fri 12/16/16
22	Final Engineering Drawings	60 days	Sat 12/17/16	Sun 2/12/17
23	City Review of Final Drawings	15 days	Sun 2/12/17	Mon 2/27/17
24	**CONSTRUCTION PLANS PERMITTING**	**196 days**	**Mon 2/27/17**	**Mon 9/4/17**
25	City of Clearwater - Site Construction Plan Approval	60 days	Mon 2/27/17	Wed 4/26/17
26	Pinellas County Public Works - R/O/W Use Permit	60 days	Mon 2/27/17	Wed 4/26/17
27	PCWMD - Commercial and Multi-use Dock Permit	90 days	Mon 2/27/17	Thu 5/25/17
28	SWFWMD - Environmental Resource Permit	90 days	Mon 2/27/17	Thu 5/25/17
29	FDEP - Water Distribution System Permit	90 days	Mon 2/27/17	Thu 5/25/17
30	FDEP - Sovereign Submerged Lands Authorization	90 days	Mon 2/27/17	Thu 5/25/17
31	USACE - Section 404 Dredge and Fill Permit	120 days	Mon 2/27/17	Fri 6/23/17
32	Responses to RAI and Resubmittals	30 days	Fri 6/23/17	Sat 7/22/17
33	Permits Issued	45 days	Sat 7/22/17	Sun 9/3/17
34	Issued for Bidding Plans Submitted to City	1 day	Sun 9/3/17	Mon 9/4/17
35	**BIDDING SERVICES**	**58 days**	**Mon 9/4/17**	**Mon 10/30/17**
36	Bidding Documents and Technical Specifications	21 days	Mon 9/4/17	Sun 9/24/17
37	Bidding Period	30 days	Sun 9/24/17	Mon 10/23/17
38	Bids Due	0 days	Mon 10/23/17	Mon 10/23/17
39	Bidding Analysis	7 days	Mon 10/23/17	Mon 10/30/17
